



GRAPEVINE – COLLEYVILLE ISD 2016 BOND & TIF PROJECT UPDATE

MARCH 25, 2019

Huckabee
MORE THAN ARCHITECTS




MULTIPURPOSE ACTIVITY CENTERS – CHHS and GHS

Huckabee
MORE THAN ARCHITECTS

MULTI-PURPOSE ACTIVITY CENTERS - CHHS & GHS

- + Joeris reports they have completed the punch list that Huckabee created with the exception of the step-down transformer for two HVAC units serving the field and the wall graphics. Huckabee will again inspect the other items on the list.**
- + Joeris' subcontractor is still working to correct the HVAC controls.**

MULTI-PURPOSE ACTIVITY CENTERS - CHHS & GHS

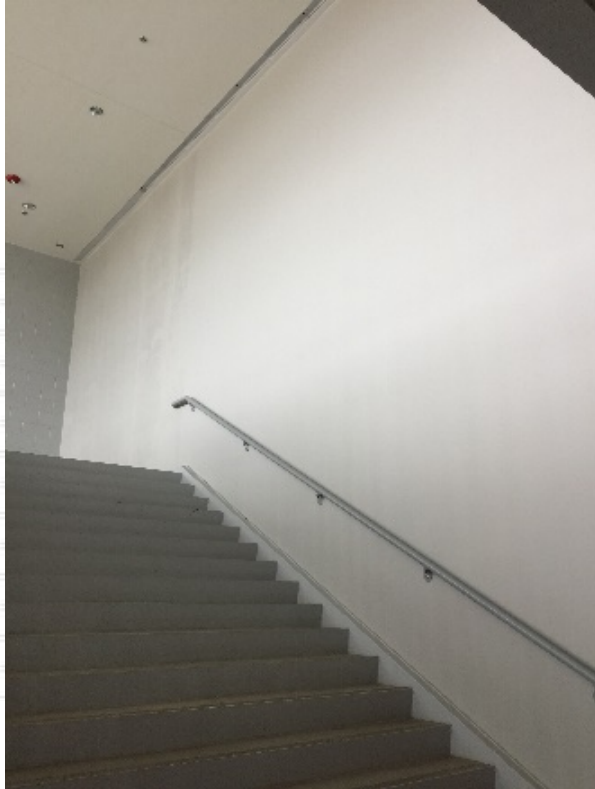

- + Walls to receive graphics were prepared the week of Spring Break.
- + Submittal for graphics to be received Monday or Tuesday of this week.

MULTI-PURPOSE ACTIVITY CENTERS - CHHS & GHS



+ Joeris has completed repairs from where the utilities were installed



CANNON ELEMENTARY SCHOOL

Huckabee
MORE THAN ARCHITECTS

CANNON ELEMENTARY SCHOOL REPLACEMENT

- + Playground benches are installed.**
- + Crushed granite installation in the garden is complete.**
- + Majority of sod around the new building is installed.**
- + The Architectural punch list has been completed and inspected by Huckabee. LLCI has been made aware of outstanding items to be completed.**
- + Need to schedule other consultants to inspect item for their lists.**

CANNON ELEMENTARY SCHOOL REPLACEMENT



- + Canopies at cafeteria have been installed.
- + Underground storm serving canopies has been installed.

CANNON ELEMENTARY SCHOOL REPLACEMENT



+ East parking lot has been constructed.

Huckabee

CANNON ELEMENTARY SCHOOL REPLACEMENT



+ The stairs and ramps are being formed for the amphitheater.

Huckabee

CANNON ELEMENTARY SCHOOL REPLACEMENT



+ Grading for the west side parking lot continues.

Huckabee

CANNON ELEMENTARY SCHOOL REPLACEMENT



+ Plaque dedicated to Mr Cannon at the front lobby entrance



MUSTANG PANTHER STADIUM RENOVATION

Huckabee
MORE THAN ARCHITECTS

MUSTANG PANTHER STADIUM RENOVATION



- + **Opening Ceremony** took place last Friday.
- + **Many items were completed** in the past two weeks. All disciplines are beginning to create punch lists.

MUSTANG PANTHER STADIUM RENOVATION



- + While operational, the sound system is still to be balanced after subwoofers are installed.
- + Lighting controls are to be integrated into the District's EMS.

A group of diverse people, including a young girl, smiling and looking at a tablet together. The image is overlaid with a red semi-transparent filter and a diamond-shaped pattern.

FIRE SUPPRESSION AND CONTROLS - GHS

Huckabee
MORE THAN ARCHITECTS

FIRE SUPPRESSION AND CONTROLS – GHS

- + The fire sprinkler scope that could be completed prior to the summer renovation work has been completed. That is in 200, 300, 400 and 600 areas.**
- + Remainder of work to coincide with Summer 2019 Renovation. Work is scheduled to begin when school year is complete.**
- + DDC control is ongoing.**



TIMBERLINE DRIVE PROJECT

Huckabee
MORE THAN ARCHITECTS

TIMBERLINE DRIVE PROJECT



- + FDC installation complete.
- + Working with city on direction for existing water meter sizing.



SUMMER 2019 RENOVATIONS

Huckabee
MORE THAN ARCHITECTS

SUMMER 2019 RENOVATIONS

- + Bids to be received on March 26, 2019 at 2:00 PM.**
- + Bids will be evaluated and scope confirmed the following week.**
- + GMP to be brought to board for approval in April.**

A group of people, including a man in a striped shirt and a woman in a dark jacket, are gathered around a table, looking at documents and a laptop. The scene is overlaid with a semi-transparent red grid pattern. The text 'Huckabee' is prominently displayed in the center, with 'MORE THAN ARCHITECTS' below it.

Huckabee

MORE THAN ARCHITECTS
