

SEPTEMBER 2018 2016 BOND & TIF PROJECT UPDATE

Grapevine-Colleyville ISD

(design plans in this document were all modified to fit budgets and do not represent current renovation work)

Huckabee



MORE THAN ARCHITECTS

Multipurpose Activity Center Updates

Timberline Elementary School Drive

Cannon Elementary School

Mustang Panther Stadium

GHS Auditorium Lighting, Sound System and Sound Room Renovation

GHS Fire Sprinkler & HVAC Controls Renovation / CHHS Fire Alarm Replacement

MULTIPURPOSE ACTIVITY CENTERS


MULTIPURPOSE ACTIVITY CENTERS CHHS & GHS

- + Contractor is currently working on punch list items at both facilities.
- + Still awaiting delivery and installation of graphics at stairwells.

GHS - MULTIPURPOSE ACTIVITY CENTERS





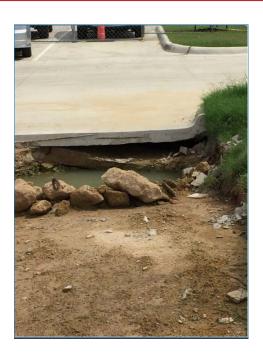

+ Parking area paving and water issues investigation ongoing.

GHS - MULTIPURPOSE ACTIVITY CENTERS







+ Parking area paving and water issues investigation ongoing.

GHS - MULTIPURPOSE ACTIVITY CENTERS







+ Drive paving and curb repairs complete by tennis courts.

TIMBERLINE ELEMENTARY SCHOOL

TES - DRIVE




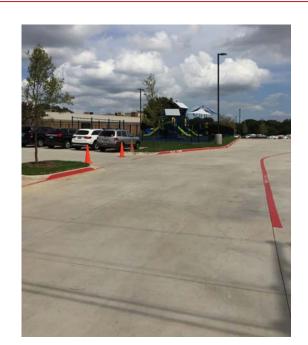


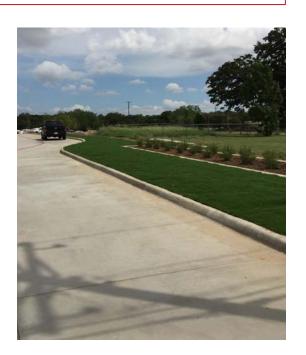

+ New drive and plantings completed

TES - DRIVE

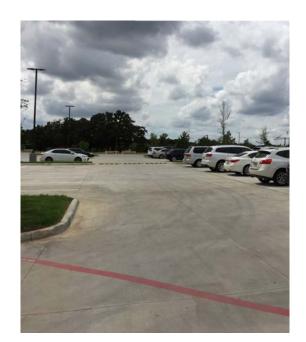

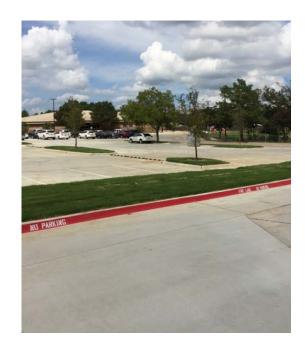




- New parking lot complete. Relocation of water line by JPS to relocate the fire riser is underway
- Civil Engineer to walk project this week

 MORE THAN ARCHITECTS

TES - PLAYGROUND

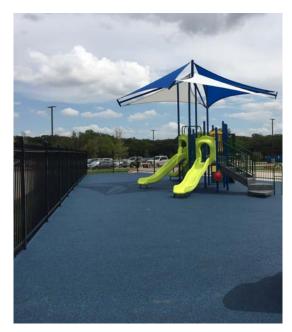






+ Playground equipment and poured in place surfacing is installed.








+ Loading dock at kitchen, sidewalk to temporary entry and curb cut on Drexel is complete.

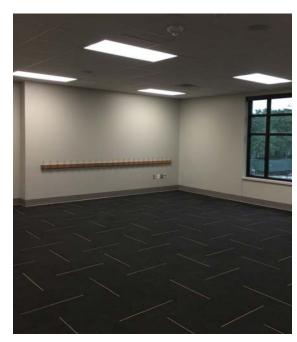

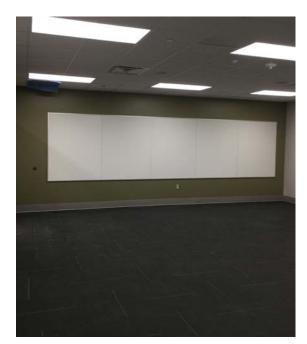




+ Typical classroom showing backpack hooks, teaching wall and entry/view to collaboration area






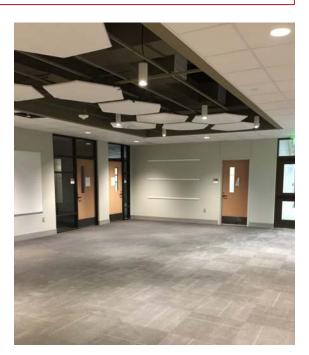


+ Typical large collaboration space outside every grade house



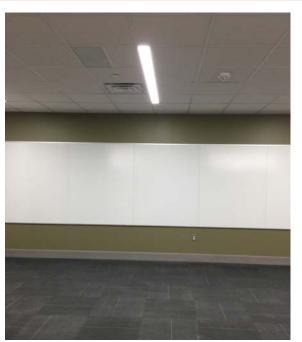




+ Typical small collaboration space shared between grade houses

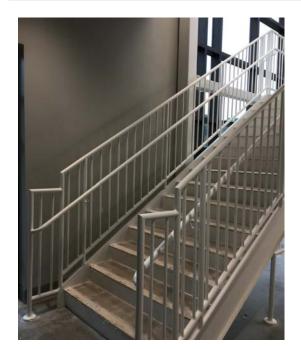





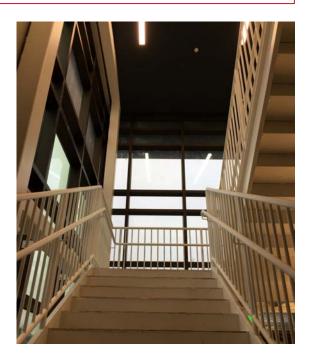


Typical stairwells at every grade house for exiting out of the building.



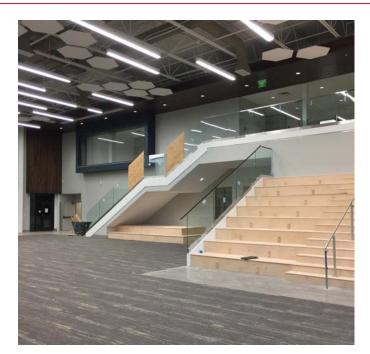


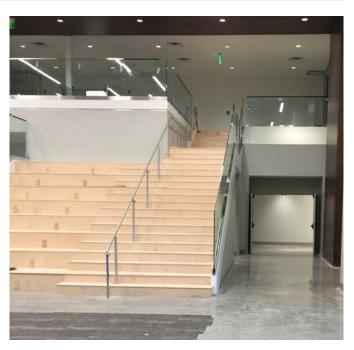

+ View of learning commons facing front entry, green room and the learning stairs

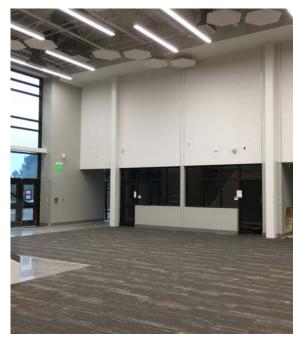




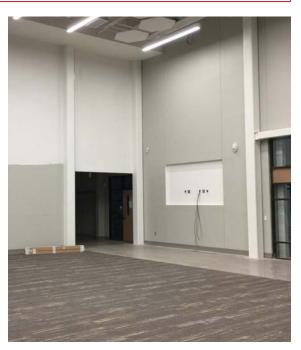

+ View of learning commons facing individual reading areas and small collaboration room.






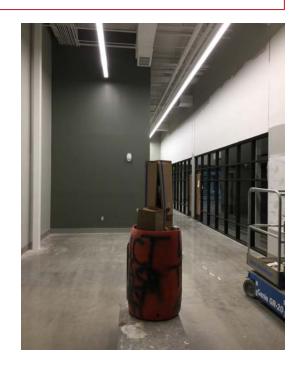

+ Robotics and the Arena Area






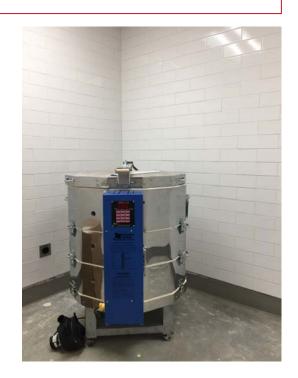

+ Art classroom with natural light and kiln room




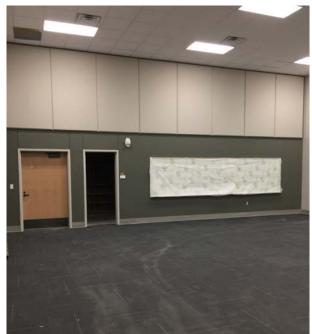



+ Music room with natural light and storage



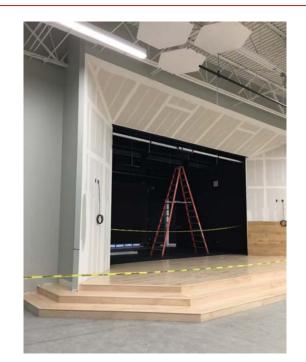




+ View of cafeteria showing the serving line, stage proscenium and booth dining seating area









+ View of kitchen serving line ready for installation and prep area, freezer/cooler and hoods installed

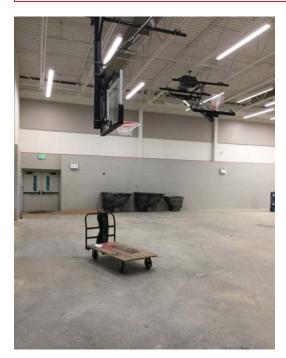

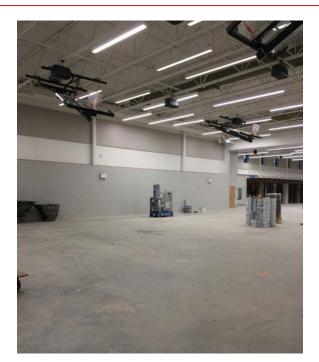

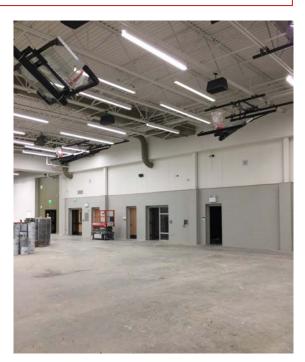

+ View of gymnasium with installed equipment and ready for flooring installation.








+ Administration area with view of reception, break-room and office corridor






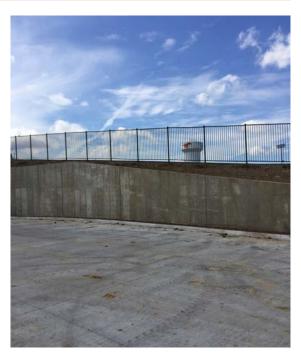

Visitor side drive is nearing completion. Stairs to mechanical pad are poured. Fence installation has begun.

MORE THAN ARCHITECTS

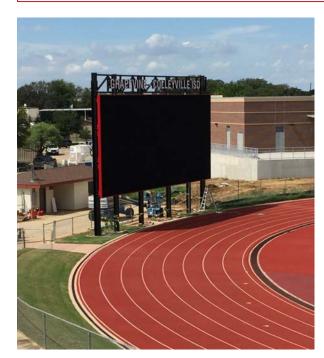



+ Scoreboard structure and display installation complete. Overall view of field side of Press Box.








North Concession with completed exterior canopy and installation of kitchen equipment is ongoing.
 MORE THAN ARCHITECTS







+ South Concession with approach drive started and stainless steel serving counter on site ready for installation.

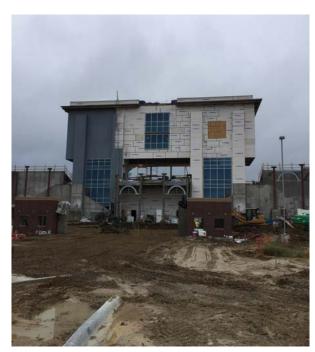





+ Press Box sheathing complete and weather barrier installation is underway. Glass at stairwells is installed. Side colonnades are being installed. Front Ticket Booths are underway.









+ Grading for the sidewalk to the new mid-level concourse on north and south ends of the stadium as well as the front approach continues


MORE THAN ARCHITECTS

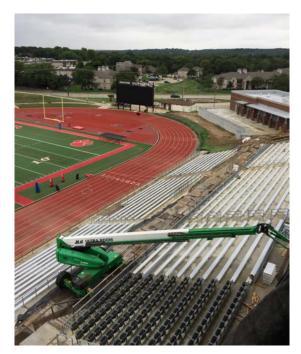

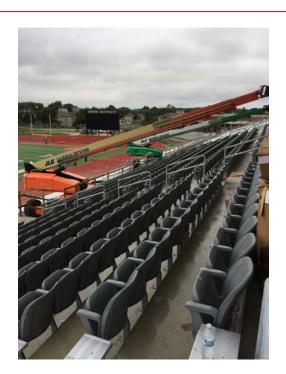



Bleacher installation is ongoing

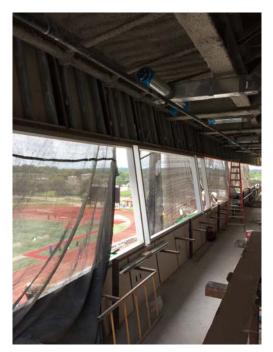





+ Framing for Press Box storefront facing field is underway. Framing for interior walls at Press Box is underway.

MORE THAN ARCHITECTS

GHS AUDITORIUM LIGHTING, SOUND AND SOUND ROOM RENOVATION

GHS LIGHTING, SOUND SYSTEM & SOUND BOOTH RENOVATION

- + Norcostco installation delayed due to supplier issues. Installation to begin this week or next.
- + Sound Room renovation scope of work brought to Board tonight for approval.
- + Commencement of scope of work will be coordinated with Theatre teacher so that disruption to the program is at a minimum.

GHS FIRE SPRINKLER & HVAC CONTROLS RENOVATION / CHHS FIRE ALARM REPLACEMENT

GHS FIRE SPRINKLER & HVAC CONTROLS RENOVATION

- + GMP finalized for GHS and brought to Board Meeting tonight for approval.
- + Work to commence in November.

SUMMER 2019 RENOVATION PROJECTS

SUMMER 2019 RENOVATION PROJECTS

- + Eight campuses to receive various renovations in the Summer of 2019:
 - Grapevine High School
 - Colleyville Middle School
 - Cross Timber Middle School
 - Dove Elementary School
 - Glennhope Elementary School
 - Grapevine Elementary School
 - O.C. Taylor Elementary School
 - Silverlake Elementary School

SUMMER 2019 RENOVATION PROJECTS

- + Current schedule:
 - 11/02: Design Development Complete
 - 01/29, 02/05, 02/12: Bid Days for Various Packages of Work
 - 03/25: GMPs Presented to Board for approval








NEW PARTITION ______


EXISTING PARTITION ______

NEW GLAZING ______

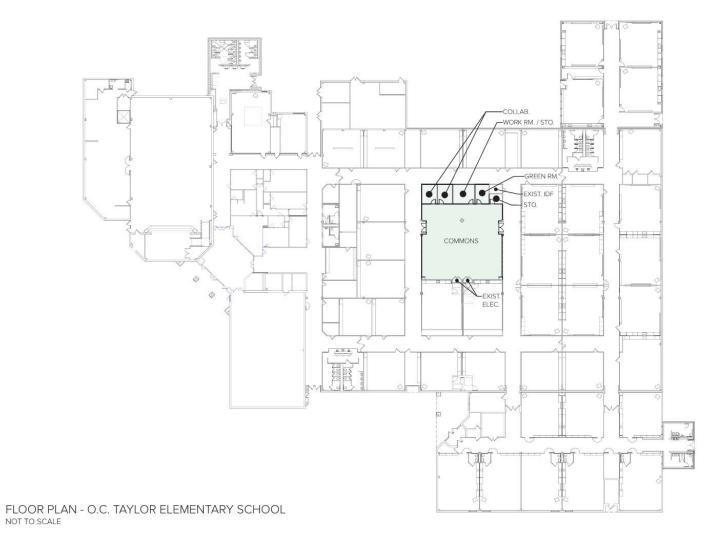

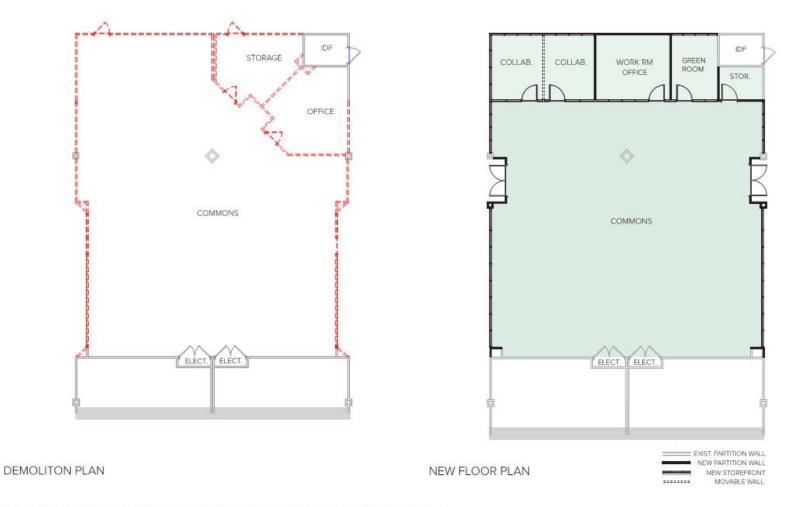

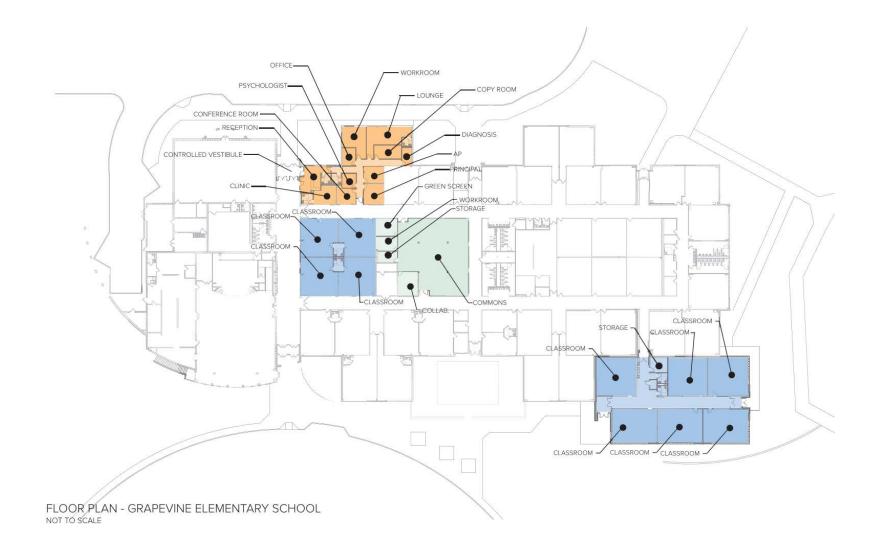

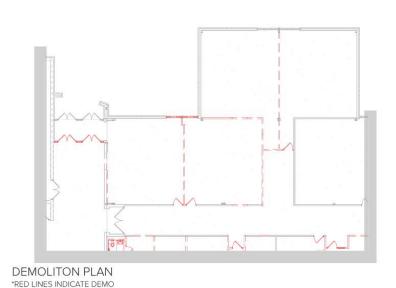




NEW FLOOR PLAN

NEW PARTITION EXISTING PARTITION NEW GLAZING




NEW GLAZING

COMMONS AND COLLABORATION SPACES - GRAPEVINE ELEMENTARY SCHOOL NOT TO SCALE

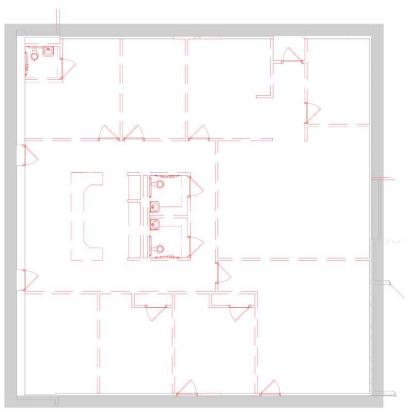

DEMOLITON PLAN *RED LINES INDICATE DEMO

ADMINISTRATION AND CLASSROOMS- GRAPEVINE ELEMENTARY SCHOOL NOT TO SCALE

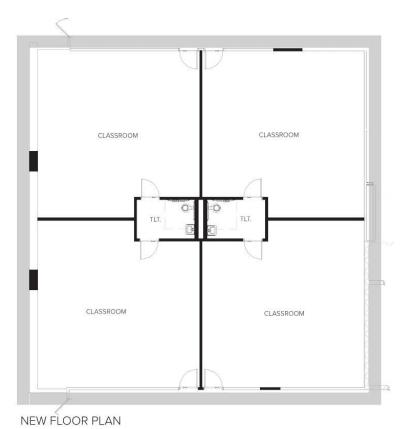

NEW PARTITION

EXISTING PARTITION


NEW GLAZING




NEW PARTITION


EXISTING PARTITION

NEW GLAZING

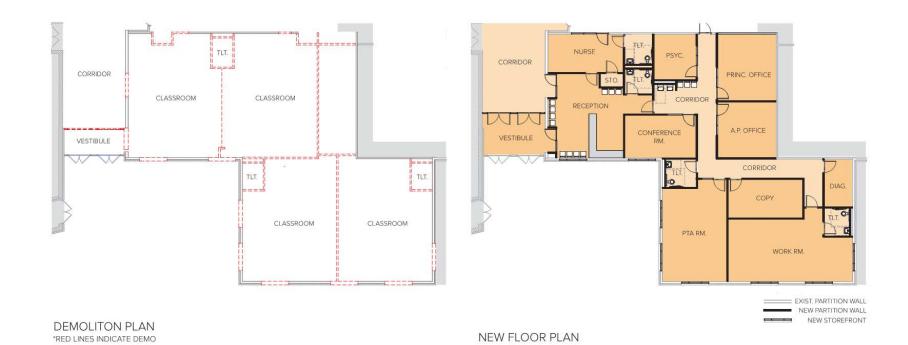


CONTROLLED VESTIBULE AND ADMINISTRATION - SILVERLAKE ELEMENTARY SCHOOL NOT TO SCALE

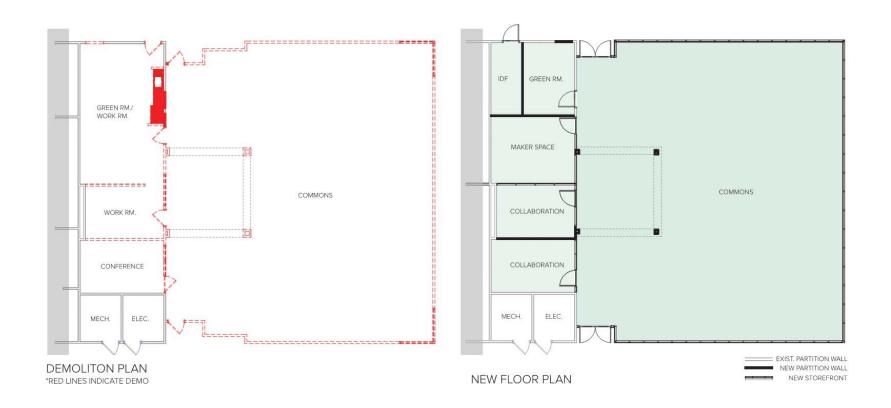


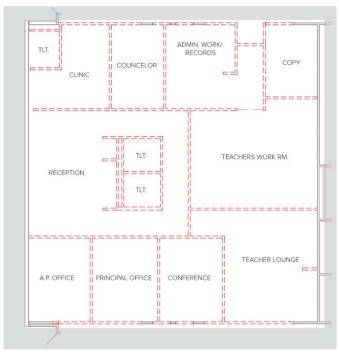




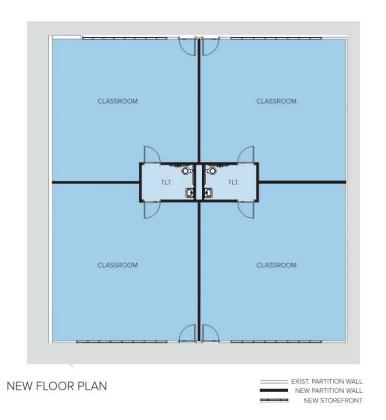



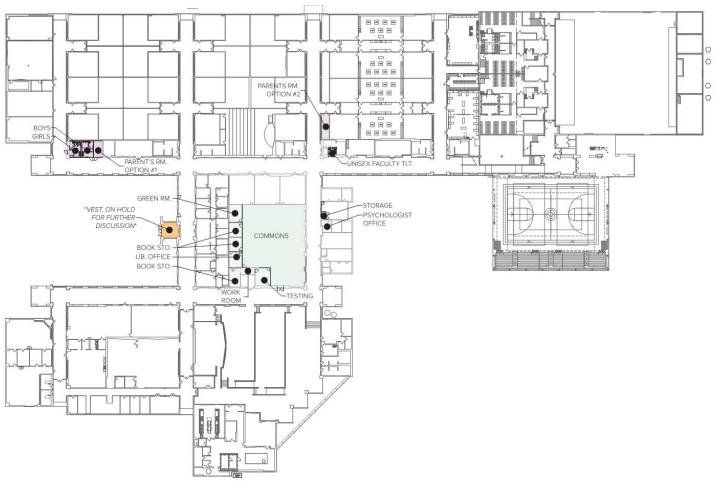

FLOOR PLAN - CROSS TIMBERS MIDDLE SCHOOL NOT TO SCALE

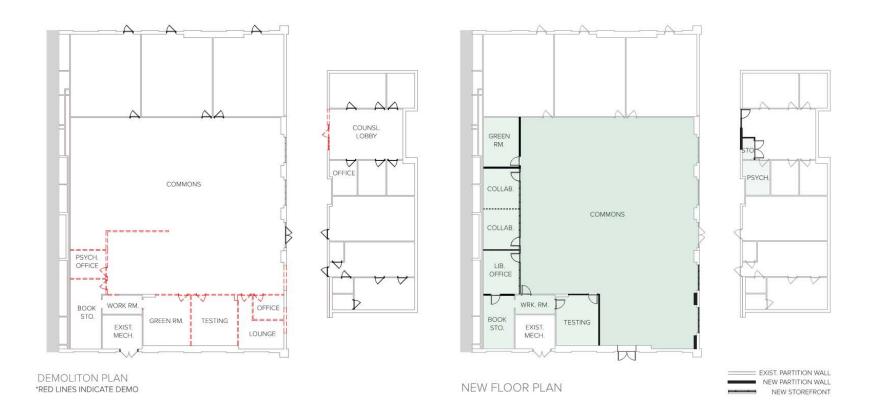










NEW FLOOR PLAN




DEMOLITON PLAN
*RED LINES INDICATE DEMO



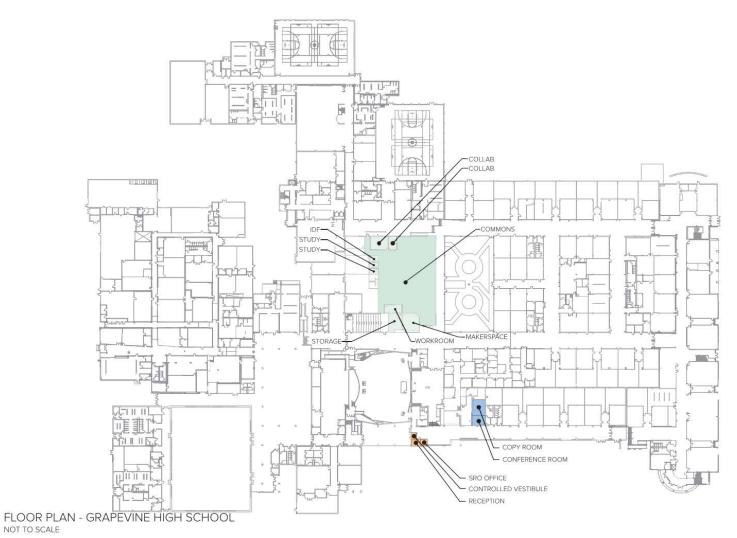



NOT TO SCALE

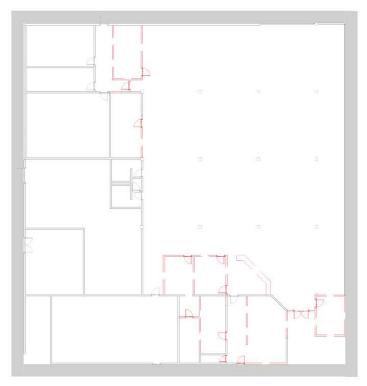


DEMOLITON PLAN

*RED LINES INDICATE DEMO

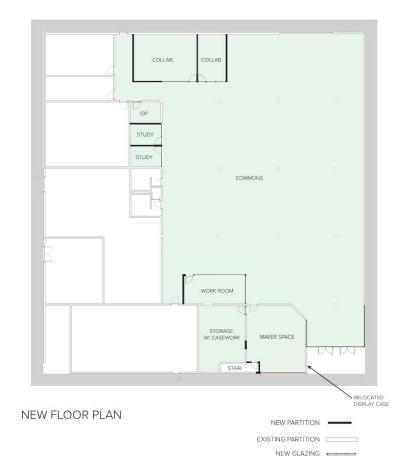

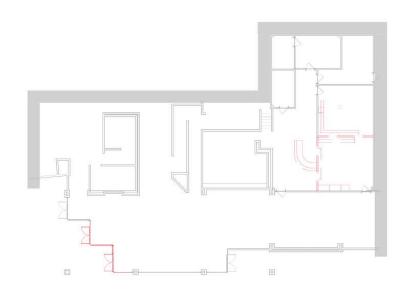

DEMOLITON PLAN
*RED LINES INDICATE DEMO

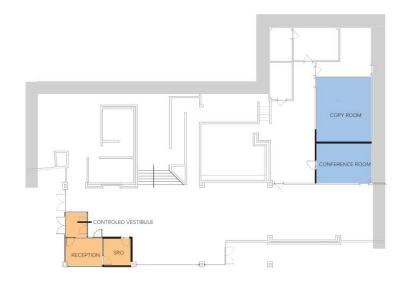

NEW FLOOR PLAN

NEW PARTITION EXISTING PARTITION

NEW GLAZING

QUESTIONS?
