



GRAPEVINE – COLLEYVILLE ISD 2016 BOND & TIF PROJECT UPDATE

MAY 20, 2019

Huckabee
MORE THAN ARCHITECTS



MULTIPURPOSE ACTIVITY CENTERS – CHHS and GHS

Huckabee
MORE THAN ARCHITECTS

MULTI-PURPOSE ACTIVITY CENTERS - CHHS & GHS

- + **Graphics for the two stairwells at each facility are in production. Joeris' subcontractor expects to install the graphics this Saturday**
- + **Joeris is working to replace dead plantings and other items on the landscape punch list including verification that the irrigation has power at CHHS**
- + **Regarding the unit heaters at the GHS MAC, a new development has led to a different investigation into the problem. Originally, the company thought the electrical run was too long and this caused the load to drop. However, most recently a unit heater closer to the panel also went out. This is being reviewed by the electrical engineer and Joeris.**
- + **Joeris is painting the red pipe railing at GHS that they replaced**
- + **Joeris is waiting on the results of cores taken from the concrete hammerheads at CHHS to assess the cracking**



CANNON ELEMENTARY SCHOOL

Huckabee
MORE THAN ARCHITECTS

CANNON ELEMENTARY SCHOOL REPLACEMENT



+ THE LIGHTED
STEPS OF THE
AMPHITHEATER
ARE BEING
FORMED AND
PREPARING FOR
POURING

Huckabee

CANNON ELEMENTARY SCHOOL REPLACEMENT



- + DIFFERENT VIEW OF THE LIGHTED STEPS OF THE AMPHITHEATER BEING FORMED AND PREPARING FOR POURING

CANNON ELEMENTARY SCHOOL REPLACEMENT



+ EAST PARKING LOT
IS STRIPED AND IN
USE

CANNON ELEMENTARY SCHOOL REPLACEMENT




- + THE TEMPORARY BUS LANE HAS BEEN REMOVED AND THE CONTRACTOR IS GRADING FOR INSTALLATION OF THE NEW EXTERIOR BASKETBALL COURT



MUSTANG PANTHER STADIUM RENOVATION

Huckabee
MORE THAN ARCHITECTS

MUSTANG PANTHER STADIUM RENOVATION

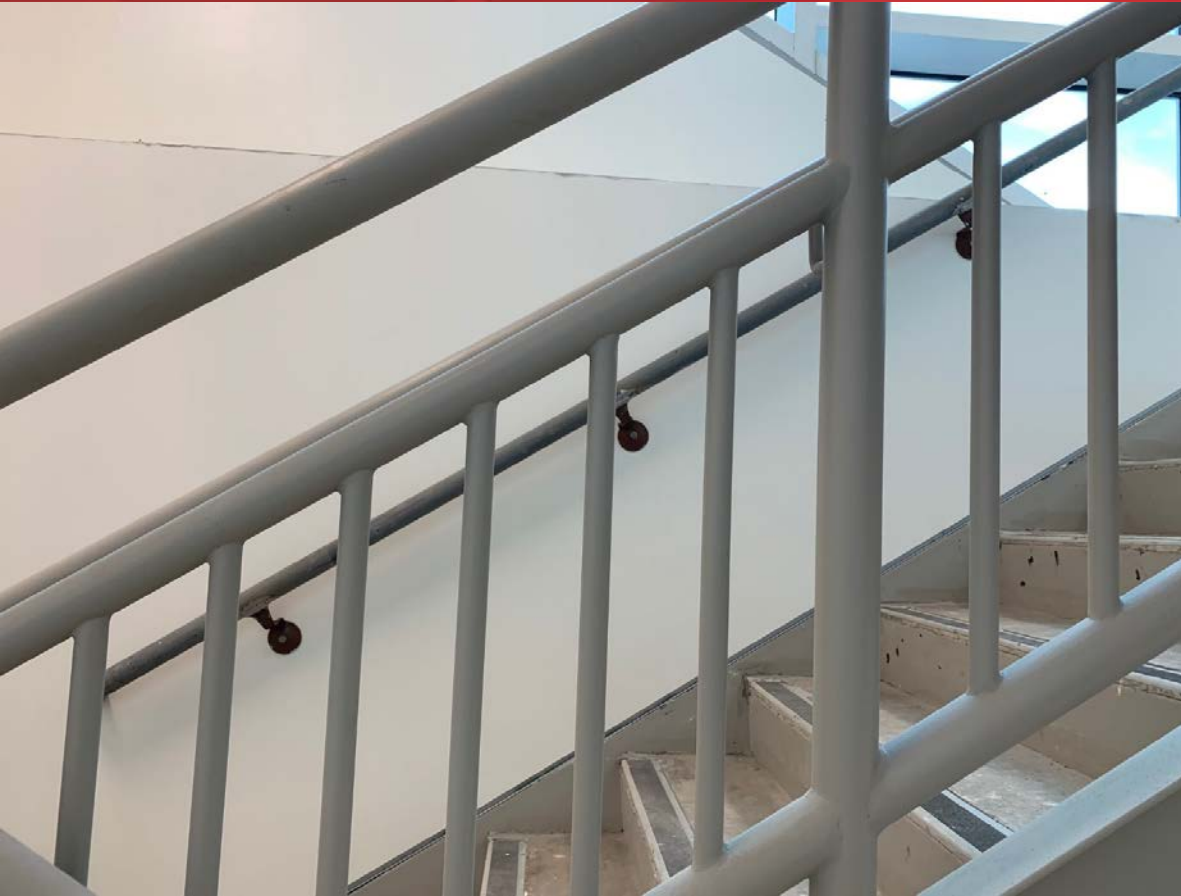

- + HANDRAILS HAVE BEEN RE-INSTALLED AT THE NORTH STAIR TOWER. STILL NEEDS TAPE, BED, TEXTURE AND PAINTING. ALSO, NEED INSTALLATION OF THE WOOD CAP AT THE SILL. THIS BEGAN THURSDAY.

Huckabee

MUSTANG PANTHER STADIUM RENOVATION



- + SOUTH STAIR TOWER LIGHT FIXTURE REINSTALLED AFTER THE LAYIN CEILING WAS ADDED. STILL NEED TAPE, BED, TEXTURE AND PAINTING. ALSO NEED INSTALLATION OF THE WOOD CAP AT THE SILL.

MUSTANG PANTHER STADIUM RENOVATION



- + LANDING ON 2ND FLOOR HAS BEEN RESLOPED TO MEET ADA/TAS REQUIREMENTS. TOPPING WILL BE REAPPLIED WITHIN A WEEK OF THE AREA DRYING OUT

MUSTANG PANTHER STADIUM RENOVATION



+ FLUMES COMPLETED
ON EACH SIDE OF
TICKET BOOTH TO
DIRECT WATER AWAY
FROM TICKET BOOTHS



TIMBERLINE DRIVE PROJECT

Huckabee
MORE THAN ARCHITECTS

TIMBERLIBE DRIVE PROJECT

- + **NEW METER WAS INSTALLED BY THE CITY**
- + **LANDSCAPER WILL BE OUT THIS WEEK TO CLEAN THE AREA**
- + **THIS PROJECT WILL THEN BE COMPLETE**



GHS PARKING LOT REVISIONS

Huckabee
MORE THAN ARCHITECTS

GHS PARKING LOT PROJECT

- + DRAWINGS HAVE BEEN SUBMITTED TO THE CITY FOR THEIR REVIEW AND ISSUANCE OF PERMIT**
- + WAITING ON REVIEW COMMENTS FROM CITY**
- + LLC IS WORKING ON REVIEWING DRAWINGS FOR PRICING TO INCLUDE IN THEIR SCOPE FOR THE SUMMER 2019 WORK**

A group of diverse people, including a young girl, smiling and looking at a tablet together. The image is overlaid with a red semi-transparent filter and a diamond-shaped grid pattern.

FIRE SUPPRESSION AND CONTROLS - GHS

Huckabee
MORE THAN ARCHITECTS

FIRE SUPPRESSION AND CONTROLS – GHS

- + BOTH FIRE SUPPRESSION AND CONTROLS WORK IS ONGOING**
- + LLC IS WORKING WITH THE PM TEAM TO STAGE THE WORK SO THAT THE TWO GYMS WILL BE AVAILABLE FOR STAGING AND STORING FURNITURE DURING THE SUMMER.**



SUMMER 2019 RENOVATIONS

Huckabee
MORE THAN ARCHITECTS

SUMMER 2019 RENOVATIONS

- + LLCI HAS PROVIDED INSURANCE AND PERFORMANCE AND PAYMENT BONDS**
- + LLCI HAS ALSO ISSUED THE SCHEDULE OF VALUES FOR THE PROJECTS FOR REVIEW**
- + THE TEAM HAD A SHOP DRAWING REVIEW SESSION ON LONG LEAD HVAC ITEMS ON 5/10/2019. ALL ITEMS WERE REVIEWED AND RETURNED TO THE CONTRACTOR**
- + HUCKABEE TEAM IS REVIEWING OTHER SUBMITTALS AS RECEIVED. IF THERE IS A NEED FOR ANOTHER EXPEDITING SUBMITTAL REVIEW, HUCKABEE IS PREPARED.**
- + BUILDING PERMITS ARE READY ON SOME OF THE PROJECTS AND THE OTHERS SHOULD BE READY SOON**

A group of people, including a man in a striped shirt and a woman in a dark jacket, are gathered around a table, looking at documents and a laptop. The scene is overlaid with a semi-transparent red grid pattern. The text "Huckabee" is prominently displayed in the center, with "MORE THAN ARCHITECTS" below it.

Huckabee

MORE THAN ARCHITECTS
